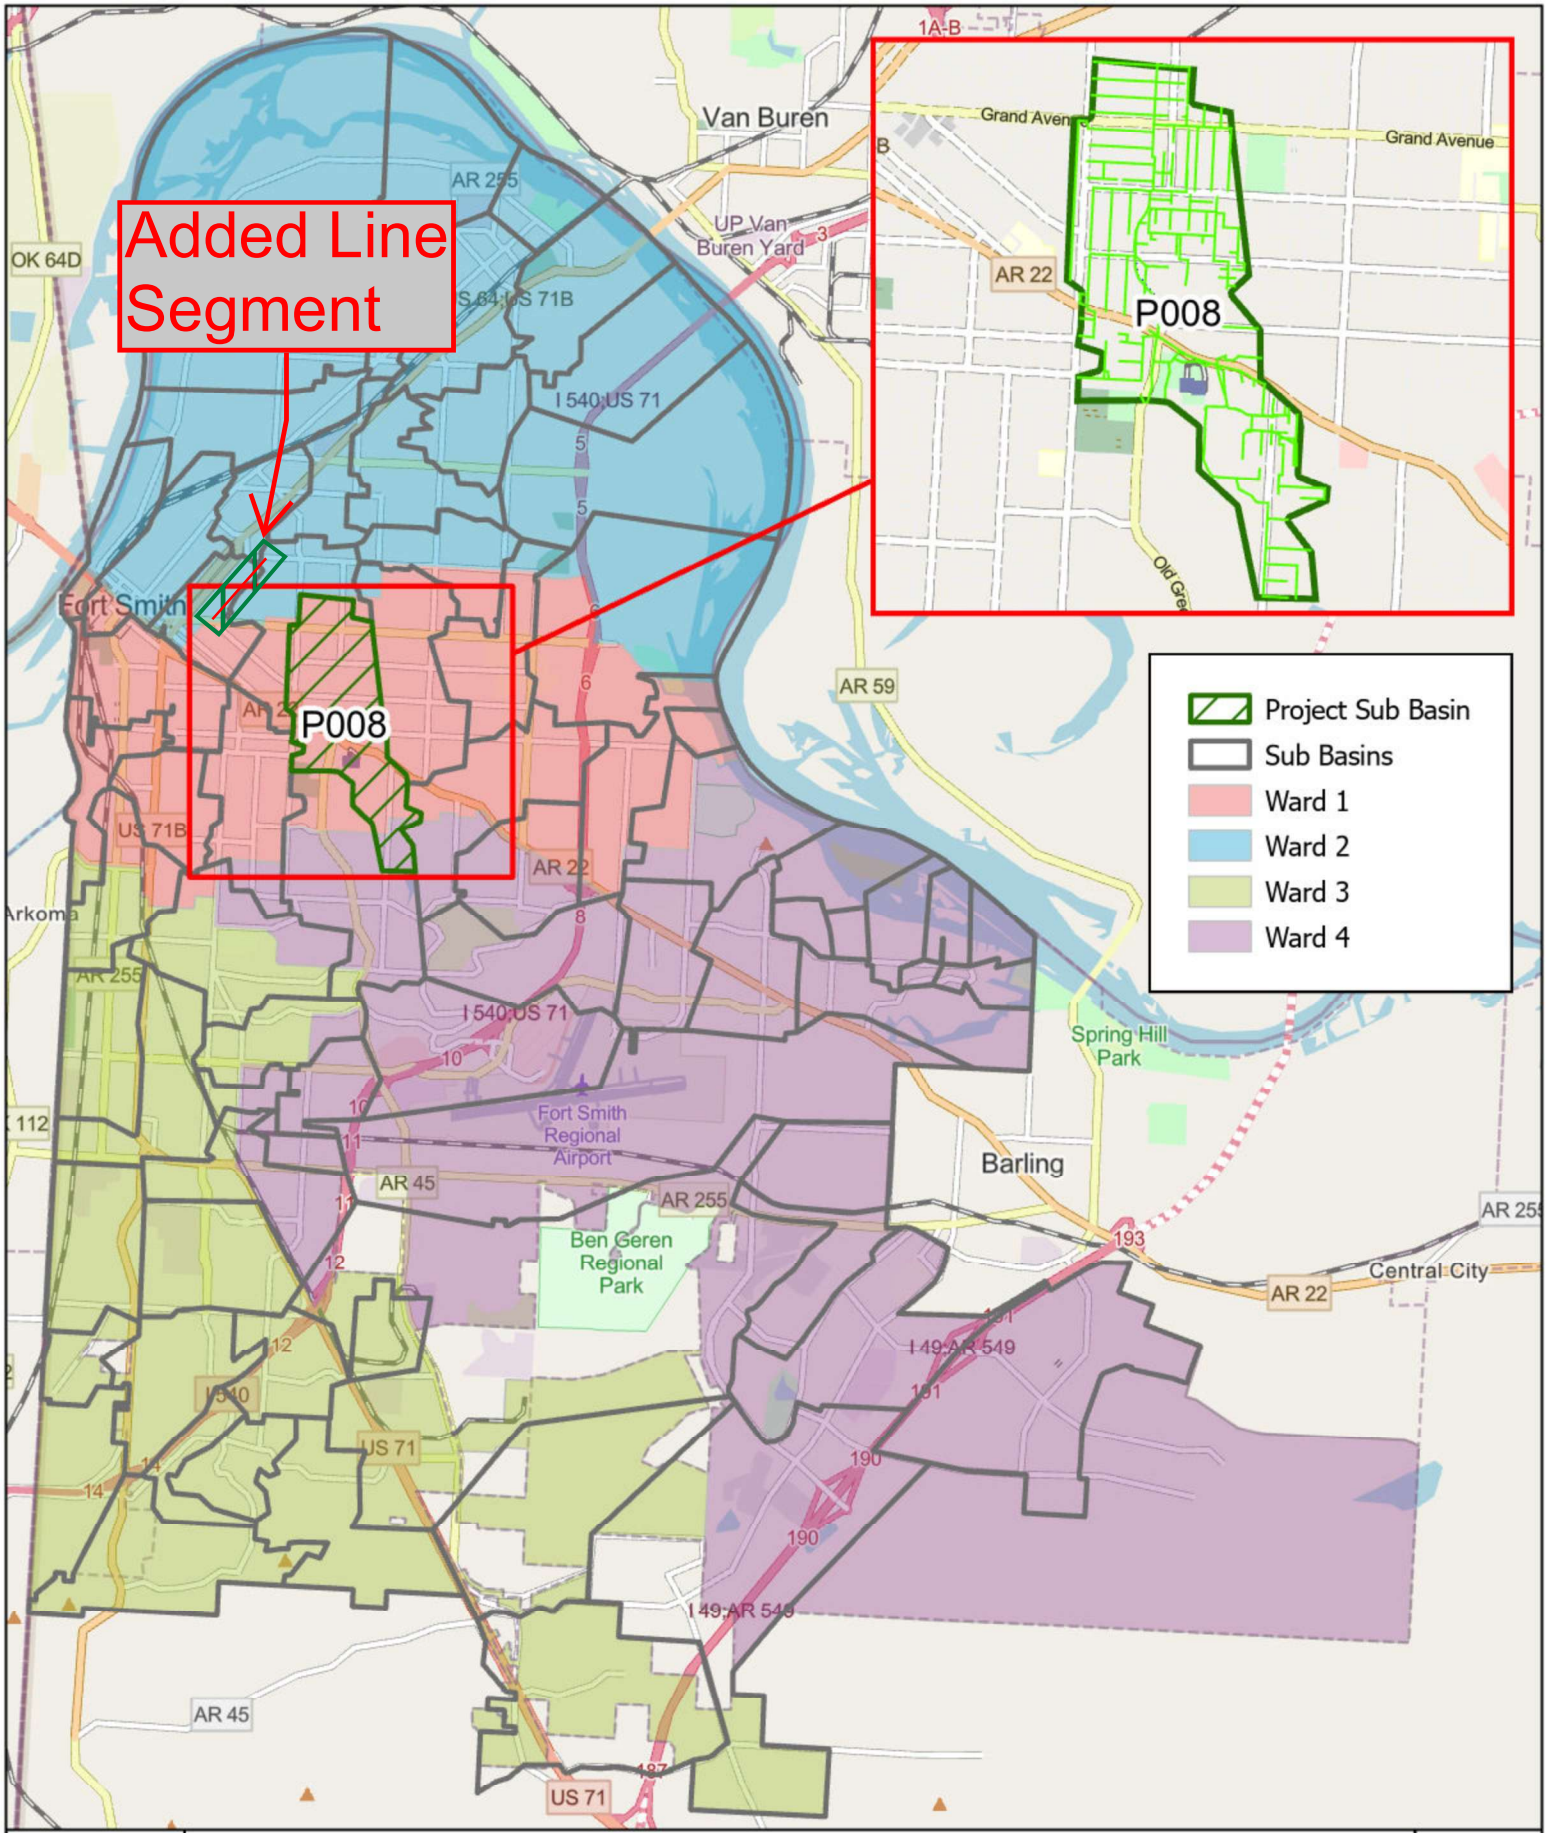


Sub-Basin

P008

17-13 - 2016 SSA Remedial Measures - Sub-Basin P008

Total Main Line Length in Project - 15,000 LF 100 Manholes

N

Project Summary

Project Name:
2016 SSA Remedial Measures, Sub-Basin P008, Phase I

Project Status:
In Progress

Project Number:
17-13-C1

Today's Date:
11/25/2026

Project Engineer:
Tyler Eldridge

Staff Contact Name:
Todd Mittge

Project Contractor:
Inliner Solutions, LLC

Staff Contact Number:
479-784-2247

Notice To Proceed Issued:
07/14/2026

Contract Breakdown		
	Dollar Amount	Contract Time (Days)
Original Contract Amount:	$6,857,019.47	450
Change Order (No. 01):	$536,706.55	60
Change Order (No. 02):		
Total Change Orders:	$536,706.55	60
Adjusted Contract:	**$7,393,726.02**	**510**

Contract Payment Breakdown		
	Dollar Amount	Percent (%)
Adjusted Contract Amount:	$7,393,726.02	
Previous Payments:	$756,410.95	
Final Payment Amount:		
Contract Balance Remaining:	**$6,637,315.07**	**89.77%**

Final Comments:
Change Order No. 1 required to incororpate future Consent Decree work on Alleyway Project into existing SSA Project.
